



Elliott Ditch Project Update

Date: October 19, 2022

Subject: Elliott Ditch Project Update No. 52


CEC Project No.: 315-052

On behalf of Arconic Lafayette, LLC (Arconic), Civil & Environmental Consultants, Inc. (CEC) is pleased to provide this status update regarding the Elliott Ditch Project. As a reminder, project status updates will be provided weekly during clean-up activities and quarterly during non-clean-up activities, at a minimum. These updates will be posted on the updates section of the Elliott Ditch Project Website (<http://elliottditchproject.cecinc.com/updates.aspx>).

Reach 3 Isolated Soil Remediation Project

- O6 Environmental (O6ENV), the remedial contractor selected by Arconic, mobilized to the Elliott Ditch Project the week of September 19, 2022, to begin Interim Measure (IM) activities.
- In advance of excavation activities, site preparation included targeted tree removal, site security, and surveying.
- Excavation activities commenced on Monday, September 26th, 2022 in the northeast corner of the remedial footprint (near S. 18th Street). Through October 19th, approximately 1,640 tons of soil have been disposed of at Republic's Chestnut Ridge disposal facility. Excavation activities are now complete within Reach 3.
- As excavation activities were performed, CEC collected confirmation samples in accordance with the IM Work Plan. Samples were submitted to a certified laboratory for analytical analysis. Re-excavation and re-sampling were performed, as necessary.
- Once acceptable sample results were achieved, O6ENV began restoring the disturbed areas. Restoration activities include backfill and topsoil installation to pre-project elevation. Sod will be planted once topsoil installation is completed.
- Arconic has secured the following permits for this IM project:
 - State of Indiana Construction Stormwater General Permit;
 - City of Lafayette Right of Way Permit;
 - City of Lafayette Site Only Permit; and,
 - Indiana Department of Natural Resources (IDNR) Construction in a Floodway Permit.
- The Interim Measures Work Plan (IMWP) summarizing this phase of the cleanup project can be found by visiting the project repository, or on IDEM's virtual file cabinet (<https://vfc.idem.in.gov/>, Document No. 83081121).
 - U.S. EPA issued approval of the IMWP on May 26, 2021.
 - IDEM issued approval of the IMWP on June 10, 2021

Should you have questions or concerns, please call the Elliott Ditch Hotline at 317-613-4514, or send an email to elliottditchquestions@gmail.com.

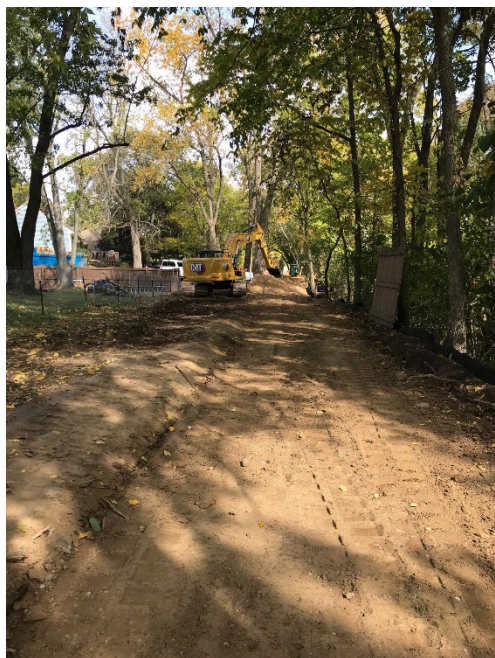

Photograph 1: Backfilling, in progress (view facing east)



Photograph 2: Backfilling, in progress (view facing west)
